



# BROADWAY STREET RECONSTRUCTION CONSTRUCTION UPDATE


**Week of April 15, 2019**



## Construction Activities

Tree removals were completed on March 30, 2019.

Construction of the underground storm sewer will begin once the Nicor's main line relocation has been completed.

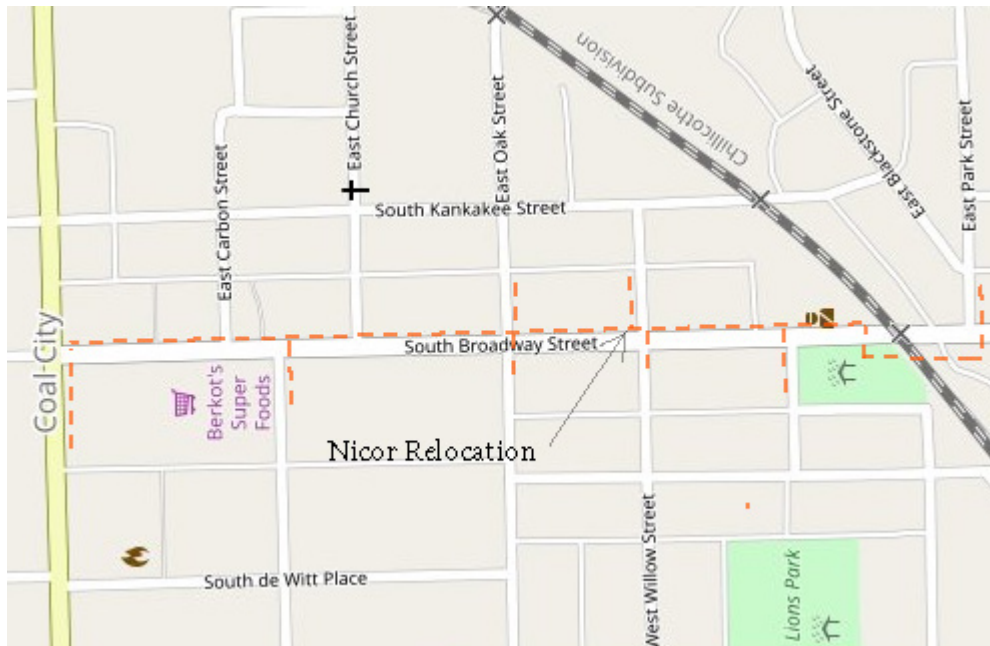

## Utility Relocation

Nicor Gas has begun relocating the gas line on Broadway from Park Street to Division. Crews are pushing the new gas line underground along the west side, which will cause some disruptions to parking and sidewalk along Broadway and the side streets. Please use caution while traveling in the area as the crews and equipment will be moving northward along Broadway.

The Nicor crews anticipate completing the main line by the week of May 13th. Nicor is anticipated to install service connection once the roadway contractor has installed portions of the new storm sewer.

VILLAGE OF COAL CITY | [WWW.COALCITY-IL.GOV](http://WWW.COALCITY-IL.GOV)

